

Weekly Update: Week of May 13, 2024

Reference: District of Ucluelet – Peninsula Road Improvements (Phase 1)

Activities for the week of May 6 to May 10:

- Peninsula Road Storm System Replacement
 - Storm Pipe – Connection at DMH #5 Completed
 - Catch Basin Installations Ongoing
- Peninsula Road Boulevard Improvements
 - Curb & Boulevard Preparation (Lyche Rd to Bay St) – Ongoing

Upcoming Activities:

- Peninsula Road Sanitary Stubs
 - Norah Road Stub – May 14
 - Peninsula Rd Crossing @ Lyche Rd – May 21/22
- Peninsula Road Boulevard Improvements
 - Curb & Boulevard Preparation – Week of May 13 & 20
 - Curb Installation – Week of May 27
 - Concrete Works – Week of June 3

See Attached Progress Photos 1 – 8



Photo #1 – Connection at DMH #5 Completed



Photo #2 – Connection at DMH #5 Completed



Photo #3 – Catch Basin Installations Ongoing

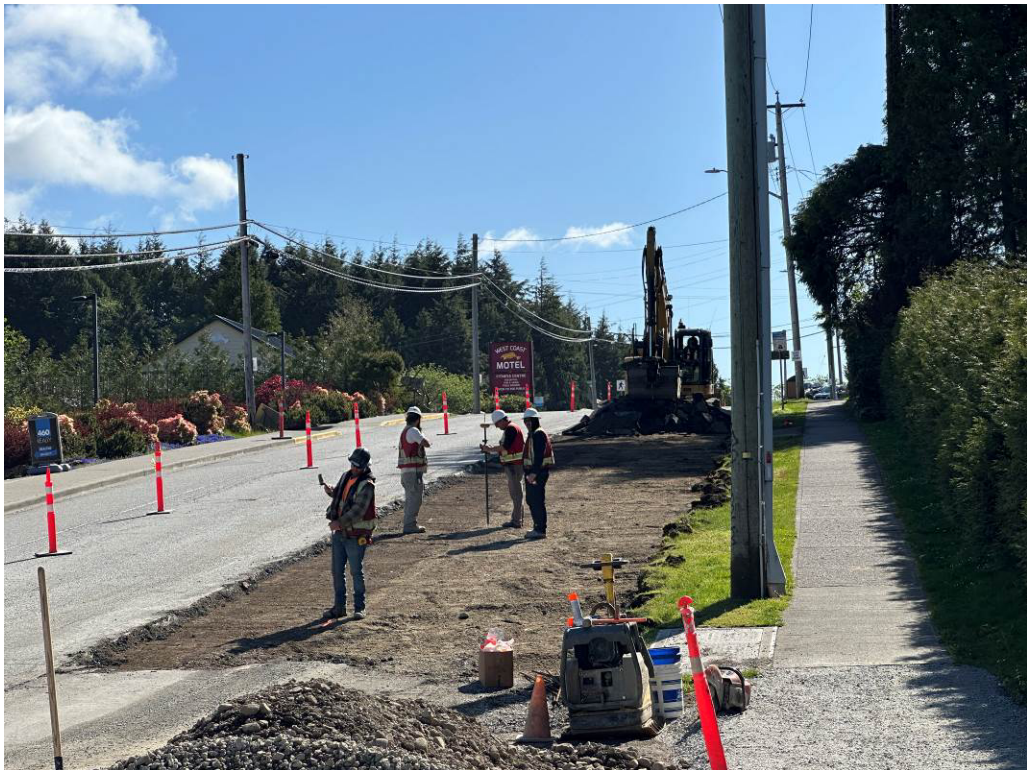


Photo #4 – Curb & Boulevard Preparation (Lyche Rd to Hemlock Rd) – Ongoing



Photo #5 – Curb & Boulevard Preparation (Lyche Rd to Hemlock Rd) – Ongoing



Photo #6 – Curb & Boulevard Preparation (Hemlock Rd to Bay St) – Ongoing



Photo #7 – Curb & Boulevard Preparation (Lyche Rd to Hemlock Rd) – Ongoing



Photo #8 – Curb & Boulevard Preparation (Lyche Rd to Hemlock Rd) – Ongoing
